


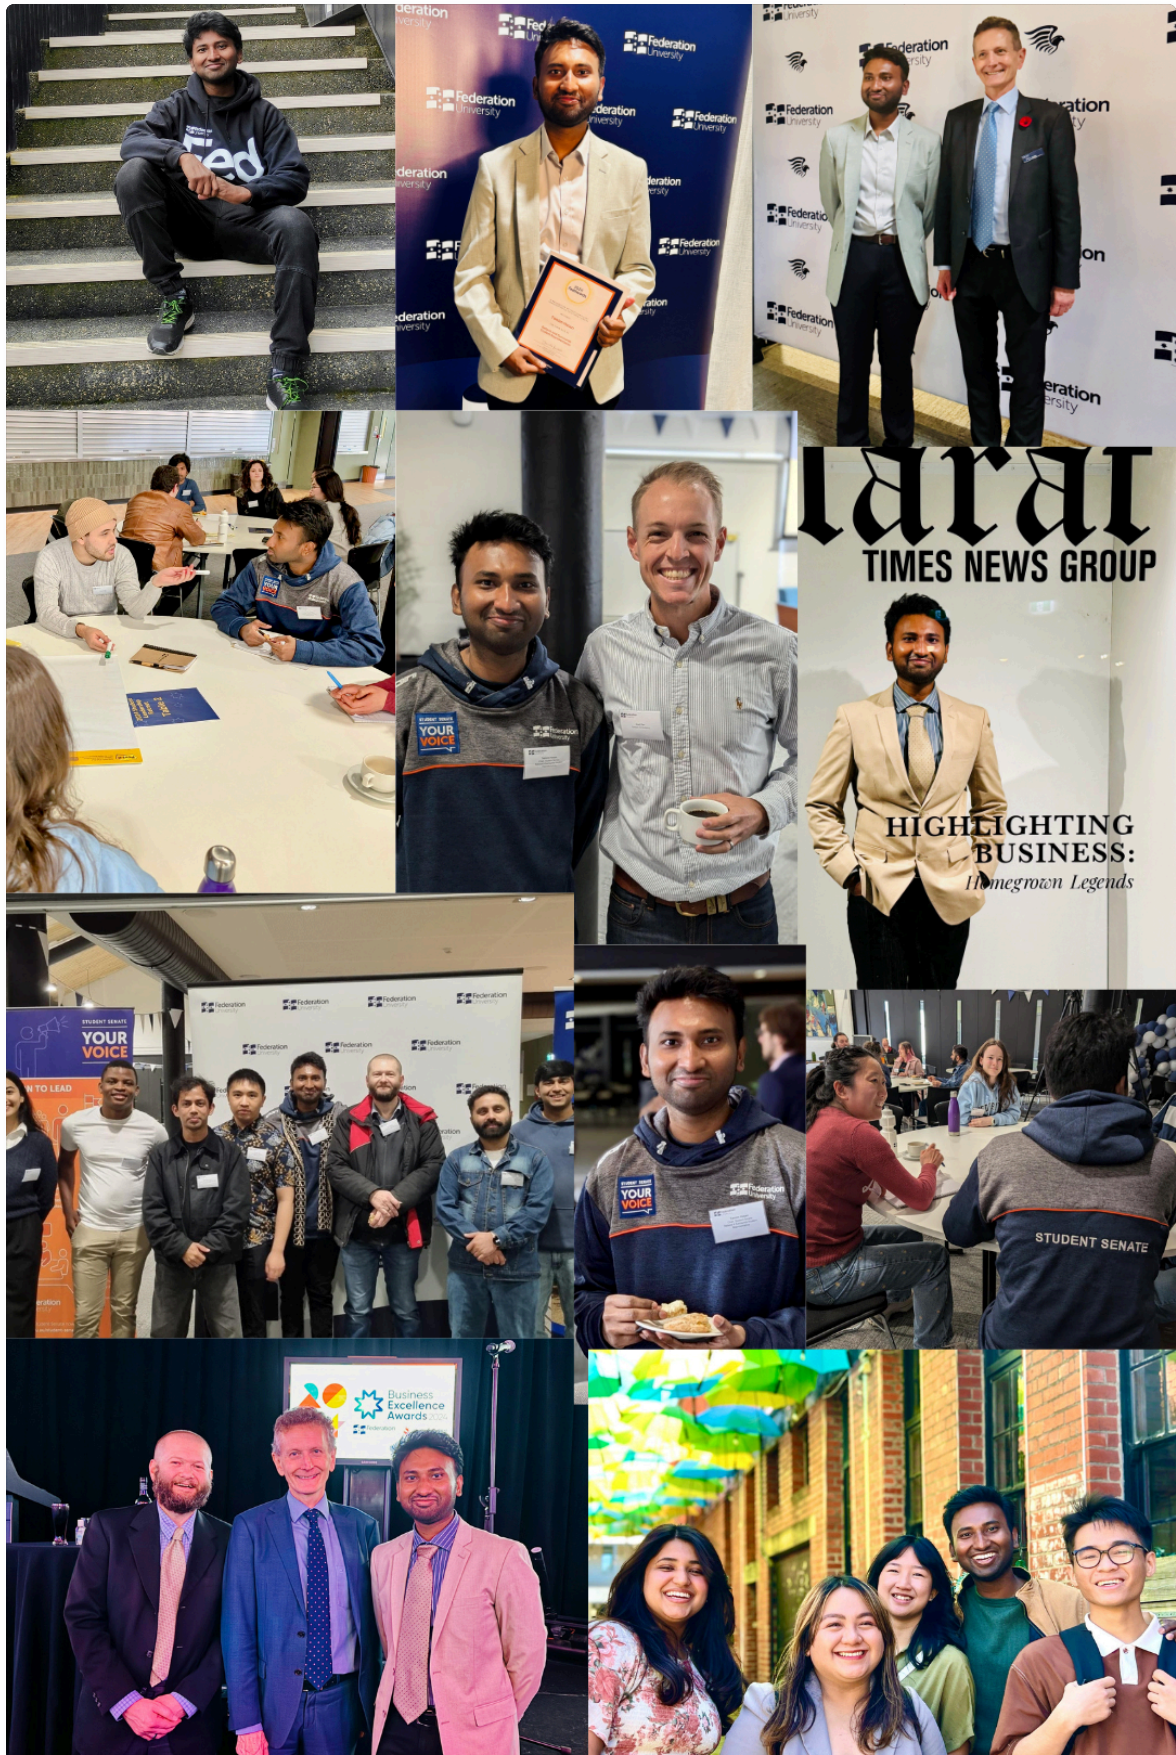

Heartland Equestrian Centre App Development

Transforming Customer Experience with a Mobile Booking Platform

Project Overview

Led the planning and development of a **mobile app for Heartland Equestrian Centre (HEC)** to improve digital engagement, streamline bookings, and modernize business operations. This app allows users to **book riding lessons, training sessions, and trail rides**, while enhancing communication and brand visibility.



HEARTLAND EQUESTRIAN CENTRE APP
DEVELOPMENT PROJECT

Role: Project Manager

As the **Project Manager**, I:

- Wrote the **executive summary** and oversaw documentation
- Designed the **Cost Model & Baseline Budget**
- Created the **Gantt Chart, Project Schedule, and Network Diagram**
- Managed **risk assessments** and stakeholder engagement
- Implemented **agile methodology** with sprints and real-time collaboration
- Coordinated project tasks and led team meetings to meet all deadlines


Team Members


- **Tamim Hasan** – Project Manager
- **Bhavani Gunnala** – Financial Analyst
- **Maricris Habana** – Technical Writer & Designer

Project Objectives


- **Develop a mobile app** for both Android and iOS
- **Enable service bookings:** lessons, trail rides, retraining
- **Provide maps, facility videos,** and interactive features
- **Collect feedback and ratings** through the app
- **Deliver 28% ROI and 2-year payback**
- **Complete project within 5 months and \$260,000 budget**

Here are some snapshots from our project–

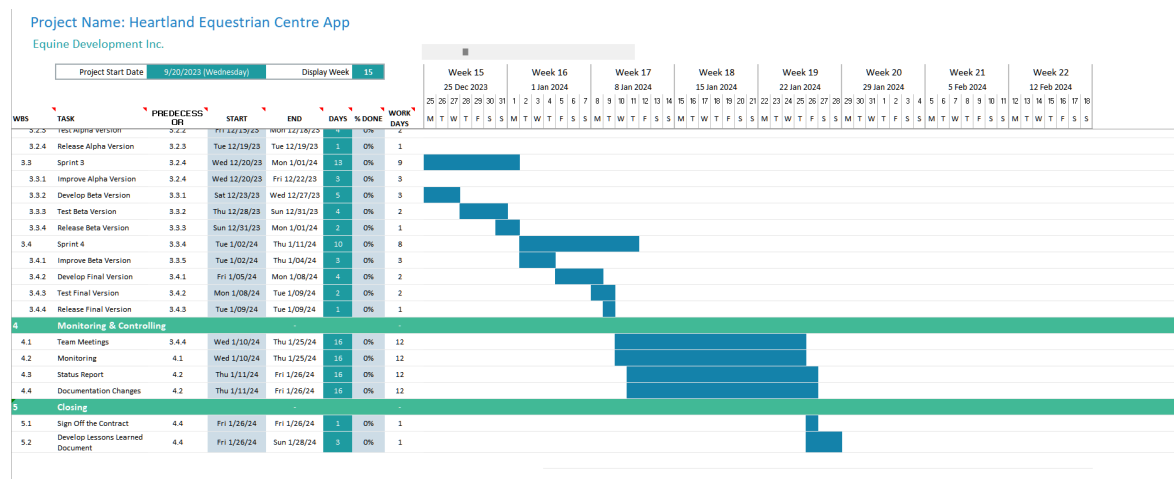

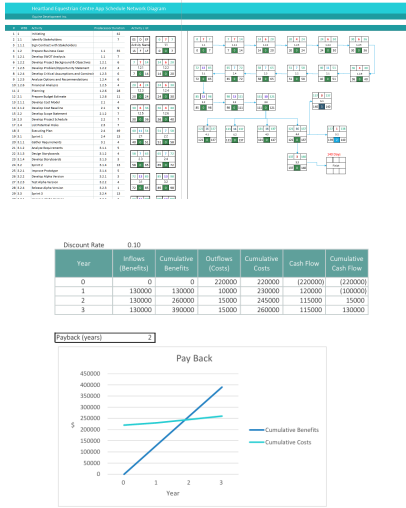

Project Name: Heartland Equestrian Centre App
Equine Development Inc.

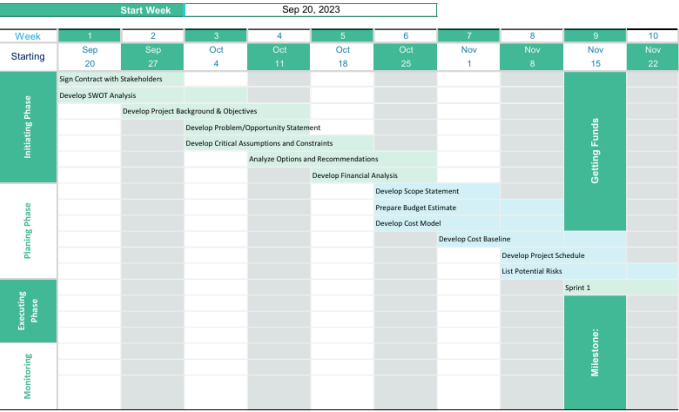

Heartland Equestrian Centre App Development Project (Budget Estimate)
Equine Development Inc.

Prepared by: Tamim Hasan		Date: 25/09/2023											
#	Expense Category	Project Expenses	Units/Hours	Cost/Unit/Hour	Subtotals	WBS Level 2 Total	Total	% of Total	Units/Hours Calculation				
									hour/day	days/week	weeks	no. team member	total hour
1	1	Initiating				\$ 4800	\$ 28800	11					
2	1.1	Identify Stakeholders											
3	1.1.1	Sign Contract with Stakeholders	40	\$ 120	\$ 4800				8	5	1	1	40
4	1.2	Prepare Business Case				\$ 24000							
5	1.2.1	Develop SWOT Analysis	40	\$ 120	\$ 4800				8	5	1	1	40
6	1.2.2	Develop Project Background & Objectives	32	\$ 120	\$ 3840				8	4	1	1	32
7	1.2.3	Develop Problem/Opportunity Statement	32	\$ 120	\$ 3840				8	4	1	1	32
8	1.2.4	Develop Critical Assumptions and Constraints	32	\$ 120	\$ 3840				8	4	1	1	32
9	1.2.5	Analyze Options and Recommendations	32	\$ 120	\$ 3840				8	4	1	1	32
10	1.2.6	Financial Analysis	32	\$ 120	\$ 3840		\$ 19200	7	8	4	1	1	32
11	2	Planning											
12	2.1	Prepare Budget Estimate				\$ 5760							
13	2.1.1	Develop Cost Model	24	\$ 120	\$ 2880				8	3	1	1	24
14	2.1.2	Develop Cost Baseline	24	\$ 120	\$ 2880				8	3	1	1	24
15	2.2	Develop Scope Statement	32	\$ 120	\$ 3840	\$ 3840			8	4	1	1	32
16	2.3	Develop Project Schedule	40	\$ 120	\$ 4800	\$ 4800			8	5	1	1	40
17	2.4	List Potential Risks	40	\$ 120	\$ 4800	\$ 4800			8	5	1	1	40
18	3	Executing Plan					\$ 73872	28					
19	3.1	Sprint 1				\$ 21384							
20	3.1.1	Gather Requirements	64.8	\$ 90	\$ 5832				7.2	3	1	3	64.8
21	3.1.2	Analyze Requirements	64.8	\$ 90	\$ 5832				7.2	3	1	3	64.8
22	3.1.3	Design Storyboards	43.2	\$ 90	\$ 3888				7.2	2	1	3	43.2
23	3.1.4	Develop Storyboards	64.8	\$ 90	\$ 5832				7.2	3	1	3	64.8
24	3.2	Sprint 2				\$ 17496							
25	3.2.1	Improve Prototype	64.8	\$ 90	\$ 5832				7.2	3	1	3	64.8
26	3.2.2	Develop Alpha Version	64.8	\$ 90	\$ 5832				7.2	3	1	3	64.8

Strategic Planning Tools Used

- **SWOT Analysis** – Evaluated internal strengths and market threats
- **Gantt Chart** – Visualized and tracked project timeline
- **Network Diagram** – Mapped task dependencies
- **Work Breakdown Structure (WBS)** – Structured project tasks
- **Risk Register** – Identified and mitigated major project risks
- **Agile Sprint Planning** – Managed sprints and collaborative tasks

Financial Highlights

- **ROI: 28%** (exceeding target of 25%)
- **Payback Period: 2 years**
- **NPV: +\$70,533** (positive investment value)

| Based on projected inflows and outflows over three years |

Artifacts

- [Full Project Report \(PDF\)](#)
- [GitHub Repository](#)

Projects

Contact

This website is designed and created by Tamim using the WordPress platform.

[View My GitHub](#)



[View My Achievements](#)
